


**2800 N. LAKE SHORE DRIVE
FACADE REPAIR PROJECT
SCHEDULE UPDATE AS OF 11/19/2025**



2800 NORTH LAKE SHORE DRIVE FACADE REPAIR PROJECT UPDATE

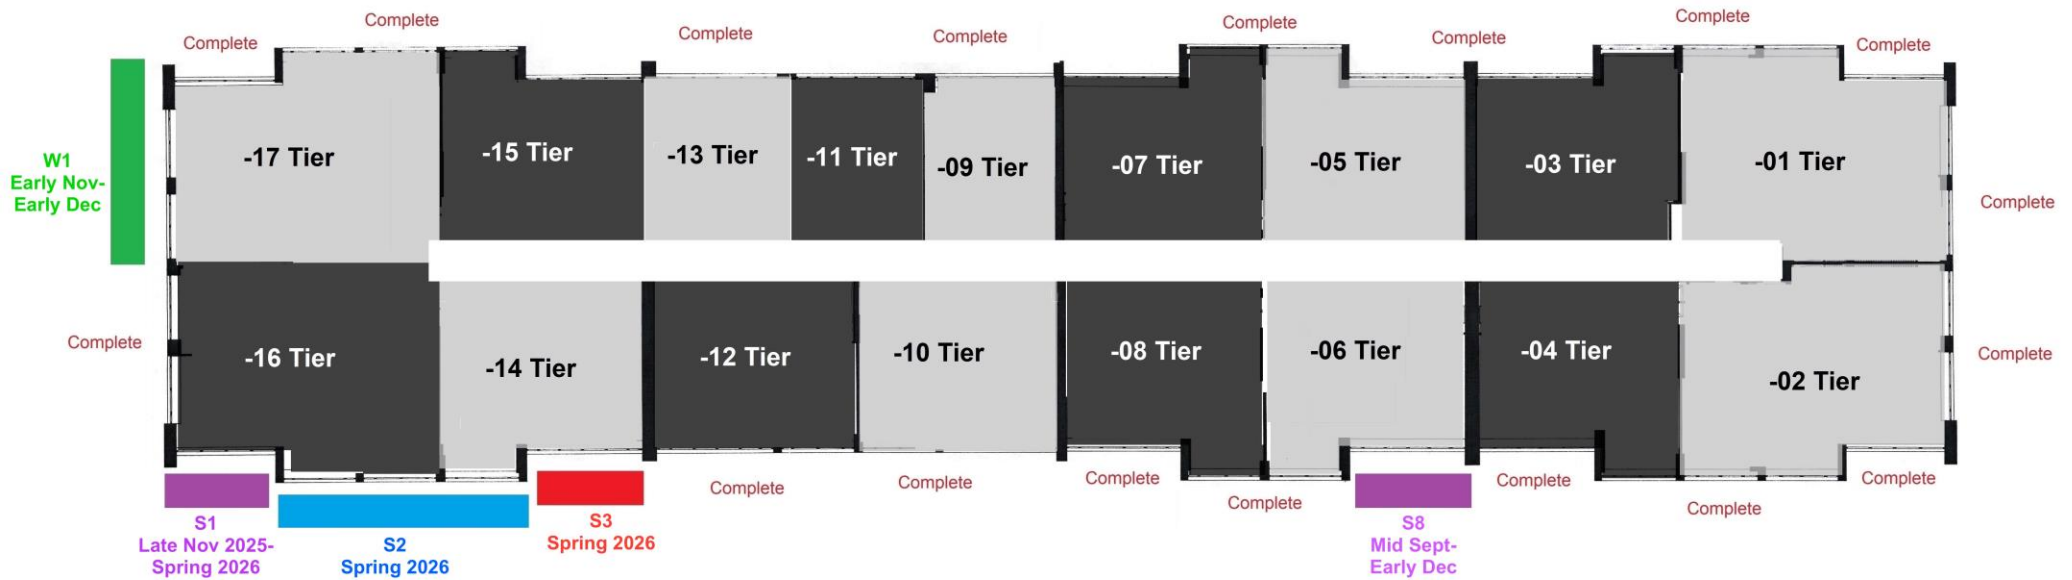

WORK SCHEDULED FOR WEEK OF 11/24 – 11/28

DROP S1:

- ~~MOBILIZATION OF EQUIPMENT~~
- **INSPECTION OF FAÇADE (SCHEDULED FOR THIS WEEK)**
- **CONCRETE DEMOLITION/REMOVAL (SCHEDULED FOR THIS WEEK)**
- CAVITY PREPARATION/FORMWORK INSTALLATION
- PLACEMENT OF CONCRETE REPAIR MATERIAL
- REMOVAL OF FORMS
- CONCRETE CRACK REPAIRS
- SEALANT REPLACEMENT/INSTALLATION
- PREPARATION OF SURFACES TO RECEIVE NEW COATINGS
- APPLICATION OF CONCRETE COATING
- FINAL INSPECTION/PUNCHLIST WORK/SHIFT STAGE TO NEXT DROP

This schedule is subject to change due to weather/wind and unforeseen circumstances.

DROP S8:

- ~~MOBILIZATION OF EQUIPMENT~~
- ~~INSPECTION OF FAÇADE~~
- ~~CONCRETE DEMOLITION/REMOVAL~~
- ~~CAVITY PREPARATION/FORMWORK INSTALLATION~~
- **PLACEMENT OF CONCRETE REPAIR MATERIAL (SCHEDULED FOR THIS WEEK)**
- **REMOVAL OF FORMS (SCHEDULED FOR THIS WEEK)**
- **CONCRETE CRACK REPAIRS (SCHEDULED FOR THIS WEEK)**
- SEALANT REPLACEMENT/INSTALLATION
- PREPARATION OF SURFACES TO RECEIVE NEW COATINGS
- APPLICATION OF CONCRETE COATING
- FINAL INSPECTION/PUNCHLIST WORK/SHIFT STAGE TO NEXT DROP

DROP W1:

- ~~MOBILIZATION OF EQUIPMENT~~
- ~~INSPECTION OF FAÇADE~~
- ~~CONCRETE DEMOLITION/REMOVAL~~
- ~~CAVITY PREPARATION/FORMWORK INSTALLATION~~
- ~~PLACEMENT OF CONCRETE REPAIR MATERIAL~~
- ~~REMOVAL OF FORMS~~
- ~~CONCRETE CRACK REPAIRS~~
- **SEALANT REPLACEMENT/INSTALLATION (SCHEDULED FOR THIS WEEK)**
- **PREPARATION OF SURFACES TO RECEIVE NEW COATINGS (SCHEDULED FOR THIS WEEK)**
- **APPLICATION OF CONCRETE COATING (SCHEDULED FOR THIS WEEK)**
- FINAL INSPECTION/PUNCHLIST WORK/SHIFT STAGE TO NEXT DROP

This schedule is subject to change due to weather/wind and unforeseen circumstances.
